



OH1400111 BLANCHESTER VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling Location	Facility ID: 1461746 SMP ID: EP002	Facility Name: BLANCHESTER STU 2 Facility Source: Surface Water	Facility Class: CLASS 3
--------------------------	---	--	--------------------------------

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.
 Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.
 Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

Chemicals	Monitoring Requirements
INORGANICS	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
ANTIMONY, TOTAL - 1074 ARSENIC - 1005 BARIUM - 1010 BERYLLIUM, TOTAL - 1075 CADMIUM - 1015 CHROMIUM - 1020 CYANIDE - 1024 FLUORIDE - 1025 MERCURY - 1035 NICKEL - 1036 SELENIUM - 1045 THALLIUM, TOTAL - 1085	
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 1/31/2020 1 Sample(s) Required between 2/1/2020 and 2/29/2020 1 Sample(s) Required between 3/1/2020 and 3/31/2020 1 Sample(s) Required between 4/1/2020 and 4/30/2020 1 Sample(s) Required between 5/1/2020 and 5/31/2020 1 Sample(s) Required between 6/1/2020 and 6/30/2020 1 Sample(s) Required between 7/1/2020 and 7/31/2020 1 Sample(s) Required between 8/1/2020 and 8/31/2020 1 Sample(s) Required between 9/1/2020 and 9/30/2020 1 Sample(s) Required between 10/1/2020 and 10/31/2020 1 Sample(s) Required between 11/1/2020 and 11/30/2020 1 Sample(s) Required between 12/1/2020 and 12/31/2020
RADIOLOGICALS	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
GROSS ALPHA - 4002 RADIUM-228 - 4030	
SYNTHETIC ORGANIC CHEMICALS (SOC) GROUP 1	1 Sample(s) Required between 4/1/2020 and 4/30/2020 1 Sample(s) Required between 5/1/2020 and 5/31/2020 1 Sample(s) Required between 6/1/2020 and 6/30/2020
<i>Sample for all the analytes listed below:</i>	
ALACHLOR (LASSO) - 2051 ATRAZINE - 2050 SIMAZINE - 2037	
VOLATILE ORGANIC CHEMICALS (VOC)	1 Sample(s) Required between 1/1/2020 and 5/31/2020
TOTAL ORGANIC CARBON (TOC)	1 Paired Sample Set Required between 1/1/2020 and 1/31/2020 1 Paired Sample Set Required between 2/1/2020 and 2/29/2020 1 Paired Sample Set Required between 3/1/2020 and 3/31/2020 1 Paired Sample Set Required between 4/1/2020 and 4/30/2020 1 Paired Sample Set Required between 5/1/2020 and 5/31/2020 1 Paired Sample Set Required between 6/1/2020 and 6/30/2020 1 Paired Sample Set Required between 7/1/2020 and 7/31/2020 1 Paired Sample Set Required between 8/1/2020 and 8/31/2020 1 Paired Sample Set Required between 9/1/2020 and 9/30/2020 1 Paired Sample Set Required between 10/1/2020 and 10/31/2020 1 Paired Sample Set Required between 11/1/2020 and 11/30/2020 1 Paired Sample Set Required between 12/1/2020 and 12/31/2020

A paired sample set refers to one source water and one treated water sample. A source water alkalinity is also required at the same time the TOC sample is taken.



Effective Date: 01/01/2020

2020 ENTRY POINT SCHEDULE

OH1400111 BLANCHESTER VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling	Facility ID: 1461746	Facility Name: BLANCHESTER STU 2	
Location	SMP ID: EP002/LT2002	Facility Source: Surface Water	Facility Class: CLASS 3

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

Chemicals

Monitoring Requirements

TOTAL MICROCYSTINS

1 Sample Set Required WEEKLY*

Total microcystins sample set refers to one raw source water sample at LT2002 and one finished water sample at EP002. A week is defined as Sunday through Saturday.

**Weekly sampling unless requirements for reduced monitoring are met. Current reduced monitoring schedules can be found at <http://epa.ohio.gov/ddagw/HAB.aspx>. Reduced monitoring is contingent on a public water system continuing to experience NO raw or finished water total microcystins detections. Any total microcystins detections during routine (weekly) or reduced sampling will trigger additional sampling. Please refer to the website above for specifics on follow-up sampling requirements.*



OH1400111 BLANCHESTER VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling	Facility ID: 1461746	Facility Name: BLANCHESTER STU 2	
Location	SMP ID: LT2002	Facility Source: Surface Water	Facility Class: CLASS 3

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

Chemicals	Monitoring Requirements
CYANOBACTERIA SCREENING	1 Sample(s) Required between 12/29/2019 and 1/4/2020
	1 Sample(s) Required between 1/12/2020 and 1/18/2020
	1 Sample(s) Required between 1/26/2020 and 2/1/2020
	1 Sample(s) Required between 2/9/2020 and 2/15/2020
	1 Sample(s) Required between 2/23/2020 and 2/29/2020
	1 Sample(s) Required between 3/8/2020 and 3/14/2020
	1 Sample(s) Required between 3/22/2020 and 3/28/2020
	1 Sample(s) Required between 4/5/2020 and 4/11/2020
	1 Sample(s) Required between 4/19/2020 and 4/25/2020
	1 Sample(s) Required between 5/3/2020 and 5/9/2020
	1 Sample(s) Required between 5/17/2020 and 5/23/2020
	1 Sample(s) Required between 5/31/2020 and 6/6/2020
	1 Sample(s) Required between 6/14/2020 and 6/20/2020
	1 Sample(s) Required between 6/28/2020 and 7/4/2020
	1 Sample(s) Required between 7/12/2020 and 7/18/2020
	1 Sample(s) Required between 7/26/2020 and 8/1/2020
	1 Sample(s) Required between 8/9/2020 and 8/15/2020
	1 Sample(s) Required between 8/23/2020 and 8/29/2020
	1 Sample(s) Required between 9/6/2020 and 9/12/2020
	1 Sample(s) Required between 9/20/2020 and 9/26/2020
1 Sample(s) Required between 10/4/2020 and 10/10/2020	
1 Sample(s) Required between 10/18/2020 and 10/24/2020	
1 Sample(s) Required between 11/1/2020 and 11/7/2020	
1 Sample(s) Required between 11/15/2020 and 11/21/2020	
1 Sample(s) Required between 11/29/2020 and 12/5/2020	
1 Sample(s) Required between 12/13/2020 and 12/19/2020	

Cyanobacteria screening sample is to be collected biweekly from raw source water at sample point LT2001 unless requirements for reduced monitoring are met. Current reduced monitoring schedules can be found at <http://epa.ohio.gov/ddagw/HAB.aspx>. As of 12/31/17, all public water systems are responsible for contracting with a lab certified to perform cyanobacteria screening (qPCR). Please review the website for further information pertaining to follow-up sampling requirements for cyanobacteria screening gene detections, and certified labs that can perform analysis.



OH1400111 BLANCHESTER VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS000	Facility Name: BLANCHESTER, VILLAGE OF DISTRIBUTION	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals	Monitoring Requirements
------------------	--------------------------------

ASBESTOS - 1094	1 Sample(s) Required between 1/1/2020 and 5/31/2020
-----------------	---

Collect one sample at a tap served by asbestos-cement pipe. Due to limited Laboratory capacity and a 48 hour filtering requirement, contact your lab early in the monitoring period to schedule a sampling date.

TOTAL COLIFORM (TCR) - 3100	5 Sample(s) Required between 1/1/2020 and 1/31/2020
	5 Sample(s) Required between 2/1/2020 and 2/29/2020
	5 Sample(s) Required between 3/1/2020 and 3/31/2020
	5 Sample(s) Required between 4/1/2020 and 4/30/2020
	5 Sample(s) Required between 5/1/2020 and 5/31/2020
	5 Sample(s) Required between 6/1/2020 and 6/30/2020
	5 Sample(s) Required between 7/1/2020 and 7/31/2020
	5 Sample(s) Required between 8/1/2020 and 8/31/2020
	5 Sample(s) Required between 9/1/2020 and 9/30/2020
	5 Sample(s) Required between 10/1/2020 and 10/31/2020
	5 Sample(s) Required between 11/1/2020 and 11/30/2020
	5 Sample(s) Required between 12/1/2020 and 12/31/2020

TOTAL CHLORINE - 1000	5 Sample(s) Required between 1/1/2020 and 1/31/2020
	5 Sample(s) Required between 2/1/2020 and 2/29/2020
	5 Sample(s) Required between 3/1/2020 and 3/31/2020
	5 Sample(s) Required between 4/1/2020 and 4/30/2020
	5 Sample(s) Required between 5/1/2020 and 5/31/2020
	5 Sample(s) Required between 6/1/2020 and 6/30/2020
	5 Sample(s) Required between 7/1/2020 and 7/31/2020
	5 Sample(s) Required between 8/1/2020 and 8/31/2020
	5 Sample(s) Required between 9/1/2020 and 9/30/2020
	5 Sample(s) Required between 10/1/2020 and 10/31/2020
	5 Sample(s) Required between 11/1/2020 and 11/30/2020
	5 Sample(s) Required between 12/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: BLANCHESTER, VILLAGE OF DISTRIBUTION 122 FAWN LANE	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals	Monitoring Requirements
------------------	--------------------------------

DISINFECTION BYPRODUCTS	Dual Sample Required between 2/8/2020 and 2/14/2020 at: DS201
	Dual Sample Required between 5/8/2020 and 5/14/2020 at: DS201
	Dual Sample Required between 8/8/2020 and 8/14/2020 at: DS201



OH1400111 BLANCHESTER VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: BLANCHESTER, VILLAGE OF DISTRIBUTION 122 FAWN LANE	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS Dual Sample Required between 11/8/2020 and 11/14/2020 at: DS201

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: BLANCHESTER, VILLAGE OF DISTRIBUTION 117 NORTHVIEW	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS

Dual Sample Required between 2/8/2020 and 2/14/2020 at: DS202

Dual Sample Required between 5/8/2020 and 5/14/2020 at: DS202

Dual Sample Required between 8/8/2020 and 8/14/2020 at: DS202

Dual Sample Required between 11/8/2020 and 11/14/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: LC###	Facility Name: BLANCHESTER, VILLAGE OF DISTRIBUTION Refer to your Lead and Copper plan for SMP IDs	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

LEAD - 1030 AND COPPER - 1022 Not Required



OH1400203 CLARKSVILLE VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1	Facility Name: CLARKSVILLE, VILLAGE OF DISTRIBUTION	Facility Class: CLASS 1
	SMP ID: DS000		

Chemicals	Monitoring Requirements
-----------	-------------------------

ASBESTOS - 1094	1 Sample(s) Required between 1/1/2020 and 5/31/2020
-----------------	---

Collect one sample at a tap served by asbestos-cement pipe. Due to limited Laboratory capacity and a 48 hour filtering requirement, contact your lab early in the monitoring period to schedule a sampling date.

TOTAL COLIFORM (TCR) - 3100	1 Sample(s) Required between 1/1/2020 and 1/31/2020
	1 Sample(s) Required between 2/1/2020 and 2/29/2020
	1 Sample(s) Required between 3/1/2020 and 3/31/2020
	1 Sample(s) Required between 4/1/2020 and 4/30/2020
	1 Sample(s) Required between 5/1/2020 and 5/31/2020
	1 Sample(s) Required between 6/1/2020 and 6/30/2020
	1 Sample(s) Required between 7/1/2020 and 7/31/2020
	1 Sample(s) Required between 8/1/2020 and 8/31/2020
	1 Sample(s) Required between 9/1/2020 and 9/30/2020
	1 Sample(s) Required between 10/1/2020 and 10/31/2020
	1 Sample(s) Required between 11/1/2020 and 11/30/2020
	1 Sample(s) Required between 12/1/2020 and 12/31/2020

TOTAL CHLORINE - 1000	1 Sample(s) Required between 1/1/2020 and 1/31/2020
	1 Sample(s) Required between 2/1/2020 and 2/29/2020
	1 Sample(s) Required between 3/1/2020 and 3/31/2020
	1 Sample(s) Required between 4/1/2020 and 4/30/2020
	1 Sample(s) Required between 5/1/2020 and 5/31/2020
	1 Sample(s) Required between 6/1/2020 and 6/30/2020
	1 Sample(s) Required between 7/1/2020 and 7/31/2020
	1 Sample(s) Required between 8/1/2020 and 8/31/2020
	1 Sample(s) Required between 9/1/2020 and 9/30/2020
	1 Sample(s) Required between 10/1/2020 and 10/31/2020
	1 Sample(s) Required between 11/1/2020 and 11/30/2020
	1 Sample(s) Required between 12/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1	Facility Name: CLARKSVILLE, VILLAGE OF DISTRIBUTION	Facility Class: CLASS 1
	SMP ID: DS201	CWWTP SPRINGHILL RD.	

Chemicals	Monitoring Requirements
-----------	-------------------------

DISINFECTION BYPRODUCTS	Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS201
-------------------------	---

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950



Effective Date: 01/01/2020

2020 DISTRIBUTION SCHEDULE

OH1400203 CLARKSVILLE VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: CLARKSVILLE, VILLAGE OF DISTRIBUTION ADDRESS NOT KNOWN	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals

Monitoring Requirements

DISINFECTION BYPRODUCTS

Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950



OH1400815 NEW VIENNA VILLAGE

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling Location	Facility ID: 1453381 SMP ID: EP001	Facility Name: NEW VIENNA WTP Facility Source: Ground Water	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

Chemicals	Monitoring Requirements
INORGANICS <i>Sample for all the analytes listed below:</i> ANTIMONY, TOTAL - 1074 ARSENIC - 1005 BARIUM - 1010 BERYLLIUM, TOTAL - 1075 CADMIUM - 1015 CHROMIUM - 1020 CYANIDE - 1024 FLUORIDE - 1025 MERCURY - 1035 NICKEL - 1036 SELENIUM - 1045 THALLIUM, TOTAL - 1085	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 5/31/2020
RADIOLOGICALS <i>Sample for all the analytes listed below:</i> GROSS ALPHA - 4002 RADIUM-228 - 4030	1 Sample(s) Required between 1/1/2020 and 5/31/2020
SYNTHETIC ORGANIC CHEMICALS (SOC) GROUP 1 <i>Sample for all the analytes listed below:</i> ALACHLOR (LASSO) - 2051 ATRAZINE - 2050 SIMAZINE - 2037	1 Sample(s) Required between 1/1/2020 and 5/31/2020
VOLATILE ORGANIC CHEMICALS (VOC)	1 Sample(s) Required between 1/1/2020 and 5/31/2020



OH1400815 NEW VIENNA VILLAGE

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS000	Facility Name: NEW VIENNA, VILLAGE OF DISTRIBUTION	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

ASBESTOS - 1094 1 Sample(s) Required between 1/1/2020 and 5/31/2020

Collect one sample at a tap served by asbestos-cement pipe. Due to limited Laboratory capacity and a 48 hour filtering requirement, contact your lab early in the monitoring period to schedule a sampling date.

TOTAL COLIFORM (TCR) - 3100

2 Sample(s) Required between 1/1/2020 and 1/31/2020

2 Sample(s) Required between 2/1/2020 and 2/29/2020

2 Sample(s) Required between 3/1/2020 and 3/31/2020

2 Sample(s) Required between 4/1/2020 and 4/30/2020

2 Sample(s) Required between 5/1/2020 and 5/31/2020

2 Sample(s) Required between 6/1/2020 and 6/30/2020

2 Sample(s) Required between 7/1/2020 and 7/31/2020

2 Sample(s) Required between 8/1/2020 and 8/31/2020

2 Sample(s) Required between 9/1/2020 and 9/30/2020

2 Sample(s) Required between 10/1/2020 and 10/31/2020

2 Sample(s) Required between 11/1/2020 and 11/30/2020

2 Sample(s) Required between 12/1/2020 and 12/31/2020

TOTAL CHLORINE - 1000

2 Sample(s) Required between 1/1/2020 and 1/31/2020

2 Sample(s) Required between 2/1/2020 and 2/29/2020

2 Sample(s) Required between 3/1/2020 and 3/31/2020

2 Sample(s) Required between 4/1/2020 and 4/30/2020

2 Sample(s) Required between 5/1/2020 and 5/31/2020

2 Sample(s) Required between 6/1/2020 and 6/30/2020

2 Sample(s) Required between 7/1/2020 and 7/31/2020

2 Sample(s) Required between 8/1/2020 and 8/31/2020

2 Sample(s) Required between 9/1/2020 and 9/30/2020

2 Sample(s) Required between 10/1/2020 and 10/31/2020

2 Sample(s) Required between 11/1/2020 and 11/30/2020

2 Sample(s) Required between 12/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: NEW VIENNA, VILLAGE OF DISTRIBUTION ADDRESS NOT KNOWN	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS201

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950



Effective Date: 01/01/2020

2020 DISTRIBUTION SCHEDULE

OH1400815 NEW VIENNA VILLAGE

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: NEW VIENNA, VILLAGE OF DISTRIBUTION ADDRESS NOT KNOWN	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: LC###	Facility Name: NEW VIENNA, VILLAGE OF DISTRIBUTION Refer to your Lead and Copper plan for SMP IDs	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

LEAD - 1030 AND COPPER - 1022 10 Sample(s) Required between 6/1/2020 and 9/30/2020

Lead consumer notice must be completed no later than two business days after receipt of the sample results. The verification form for consumer notice must be submitted to Ohio EPA no later than five business days after receipt of the sample results. Lead and copper sample monitoring point (SMP) IDs (LC###) must be current and reflect properly tiered sites according to OAC Rule 3745-81-86. Submit lead and copper SMP ID revisions to your Ohio EPA District Office. Forms and templates are available online at <http://epa.ohio.gov/ddagw/pws/leadandcopper.aspx>. For questions contact your Ohio EPA District Office representative.



Effective Date: 01/01/2020

2020 ENTRY POINT SCHEDULE

OH1400912 SABINA VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling Location	Facility ID: 1453382 SMP ID: EP001	Facility Name: SABINA VILLAGE Facility Source: Ground Water	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

Chemicals	Monitoring Requirements
INORGANICS <i>Sample for all the analytes listed below:</i> ANTIMONY, TOTAL - 1074 ARSENIC - 1005 BARIUM - 1010 BERYLLIUM, TOTAL - 1075 CADMIUM - 1015 CHROMIUM - 1020 CYANIDE - 1024 FLUORIDE - 1025 MERCURY - 1035 NICKEL - 1036 SELENIUM - 1045 THALLIUM, TOTAL - 1085	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 5/31/2020
RADIOLOGICALS <i>Sample for all the analytes listed below:</i> GROSS ALPHA - 4002 RADIUM-228 - 4030	1 Sample(s) Required between 1/1/2020 and 5/31/2020
SYNTHETIC ORGANIC CHEMICALS (SOC) GROUP 1 <i>Sample for all the analytes listed below:</i> ALACHLOR (LASSO) - 2051 ATRAZINE - 2050 SIMAZINE - 2037	1 Sample(s) Required between 1/1/2020 and 5/31/2020
VOLATILE ORGANIC CHEMICALS (VOC)	1 Sample(s) Required between 1/1/2020 and 5/31/2020



OH1400912 SABINA VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS000	Facility Name: SABINA, VILLAGE OF DISTRIBUTION	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals	Monitoring Requirements
-----------	-------------------------

ASBESTOS - 1094	1 Sample(s) Required between 1/1/2020 and 5/31/2020
-----------------	---

Collect one sample at a tap served by asbestos-cement pipe. Due to limited Laboratory capacity and a 48 hour filtering requirement, contact your lab early in the monitoring period to schedule a sampling date.

TOTAL COLIFORM (TCR) - 3100	3 Sample(s) Required between 1/1/2020 and 1/31/2020
	3 Sample(s) Required between 2/1/2020 and 2/29/2020
	3 Sample(s) Required between 3/1/2020 and 3/31/2020
	3 Sample(s) Required between 4/1/2020 and 4/30/2020
	3 Sample(s) Required between 5/1/2020 and 5/31/2020
	3 Sample(s) Required between 6/1/2020 and 6/30/2020
	3 Sample(s) Required between 7/1/2020 and 7/31/2020
	3 Sample(s) Required between 8/1/2020 and 8/31/2020
	3 Sample(s) Required between 9/1/2020 and 9/30/2020
	3 Sample(s) Required between 10/1/2020 and 10/31/2020
	3 Sample(s) Required between 11/1/2020 and 11/30/2020
	3 Sample(s) Required between 12/1/2020 and 12/31/2020

TOTAL CHLORINE - 1000	3 Sample(s) Required between 1/1/2020 and 1/31/2020
	3 Sample(s) Required between 2/1/2020 and 2/29/2020
	3 Sample(s) Required between 3/1/2020 and 3/31/2020
	3 Sample(s) Required between 4/1/2020 and 4/30/2020
	3 Sample(s) Required between 5/1/2020 and 5/31/2020
	3 Sample(s) Required between 6/1/2020 and 6/30/2020
	3 Sample(s) Required between 7/1/2020 and 7/31/2020
	3 Sample(s) Required between 8/1/2020 and 8/31/2020
	3 Sample(s) Required between 9/1/2020 and 9/30/2020
	3 Sample(s) Required between 10/1/2020 and 10/31/2020
	3 Sample(s) Required between 11/1/2020 and 11/30/2020
	3 Sample(s) Required between 12/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: SABINA, VILLAGE OF DISTRIBUTION ADDRESS NOT KNOWN	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals	Monitoring Requirements
-----------	-------------------------

DISINFECTION BYPRODUCTS	Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS201
-------------------------	---

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950



OH1400912 SABINA VILLAGE PWS

System Type: Community

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: SABINA, VILLAGE OF DISTRIBUTION ADDRESS NOT KNOWN	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS Dual Sample Required between 7/1/2020 and 9/30/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: LC###	Facility Name: SABINA, VILLAGE OF DISTRIBUTION Refer to your Lead and Copper plan for SMP IDs	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

LEAD - 1030 AND COPPER - 1022 10 Sample(s) Required between 6/1/2020 and 9/30/2020

Lead consumer notice must be completed no later than two business days after receipt of the sample results. The verification form for consumer notice must be submitted to Ohio EPA no later than five business days after receipt of the sample results. Lead and copper sample monitoring point (SMP) IDs (LC###) must be current and reflect properly tiered sites according to OAC Rule 3745-81-86. Submit lead and copper SMP ID revisions to your Ohio EPA District Office. Forms and templates are available online at <http://epa.ohio.gov/ddagw/pws/leadandcopper.aspx>. For questions contact your Ohio EPA District Office representative.



OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling Location	Facility ID: 1453383 SMP ID: EP001	Facility Name: WILMINGTON WATER DEPARTMENT Facility Source: Surface Water	Facility Class: CLASS 3
--------------------------	---	--	--------------------------------

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

Chemicals	Monitoring Requirements
INORGANICS	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
ANTIMONY, TOTAL - 1074 ARSENIC - 1005 BARIUM - 1010 BERYLLIUM, TOTAL - 1075 CADMIUM - 1015 CHROMIUM - 1020 CYANIDE - 1024 FLUORIDE - 1025 MERCURY - 1035 NICKEL - 1036 SELENIUM - 1045 THALLIUM, TOTAL - 1085	
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 1/31/2020 1 Sample(s) Required between 2/1/2020 and 2/29/2020 1 Sample(s) Required between 3/1/2020 and 3/31/2020 1 Sample(s) Required between 4/1/2020 and 4/30/2020 1 Sample(s) Required between 5/1/2020 and 5/31/2020 1 Sample(s) Required between 6/1/2020 and 6/30/2020 1 Sample(s) Required between 7/1/2020 and 7/31/2020 1 Sample(s) Required between 8/1/2020 and 8/31/2020 1 Sample(s) Required between 9/1/2020 and 9/30/2020 1 Sample(s) Required between 10/1/2020 and 10/31/2020 1 Sample(s) Required between 11/1/2020 and 11/30/2020 1 Sample(s) Required between 12/1/2020 and 12/31/2020
RADIOLOGICALS	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
GROSS ALPHA - 4002 RADIUM-228 - 4030	
SYNTHETIC ORGANIC CHEMICALS (SOC) GROUP 1	1 Sample(s) Required between 4/1/2020 and 6/30/2020
<i>Sample for all the analytes listed below:</i>	
ALACHLOR (LASSO) - 2051 ATRAZINE - 2050 SIMAZINE - 2037	
VOLATILE ORGANIC CHEMICALS (VOC)	1 Sample(s) Required between 1/1/2020 and 5/31/2020
TOTAL ORGANIC CARBON (TOC)	1 Paired Sample Set Required between 1/1/2020 and 1/31/2020 1 Paired Sample Set Required between 2/1/2020 and 2/29/2020 1 Paired Sample Set Required between 3/1/2020 and 3/31/2020 1 Paired Sample Set Required between 4/1/2020 and 4/30/2020 1 Paired Sample Set Required between 5/1/2020 and 5/31/2020 1 Paired Sample Set Required between 6/1/2020 and 6/30/2020 1 Paired Sample Set Required between 7/1/2020 and 7/31/2020 1 Paired Sample Set Required between 8/1/2020 and 8/31/2020 1 Paired Sample Set Required between 9/1/2020 and 9/30/2020 1 Paired Sample Set Required between 10/1/2020 and 10/31/2020 1 Paired Sample Set Required between 11/1/2020 and 11/30/2020 1 Paired Sample Set Required between 12/1/2020 and 12/31/2020

A paired sample set refers to one source water and one treated water sample. A source water alkalinity is also required at the same time the TOC sample is taken.



Effective Date: 01/01/2020

2020 ENTRY POINT SCHEDULE

OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling	Facility ID: 1453383	Facility Name: WILMINGTON WATER DEPARTMENT
Location	SMP ID: EP001/LT2001	Facility Source: Surface Water
		Facility Class: CLASS 3

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

**** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020**

Chemicals

Monitoring Requirements

TOTAL MICROCYSTINS

1 Sample Set Required WEEKLY*

Total microcystins sample set refers to one raw source water sample at LT2001 and one finished water sample at EP001. A week is defined as Sunday through Saturday.

**Weekly sampling unless requirements for reduced monitoring are met. Current reduced monitoring schedules can be found at <http://epa.ohio.gov/ddagw/HAB.aspx>. Reduced monitoring is contingent on a public water system continuing to experience NO raw or finished water total microcystins detections. Any total microcystins detections during routine (weekly) or reduced sampling will trigger additional sampling. Please refer to the website above for specifics on follow-up sampling requirements.*



OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling	Facility ID: 1453383	Facility Name: WILMINGTON WATER DEPARTMENT
Location	SMP ID: LT2001	Facility Source: Surface Water
		Facility Class: CLASS 3

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

Chemicals	Monitoring Requirements
CYANOBACTERIA SCREENING	1 Sample(s) Required between 12/29/2019 and 1/4/2020
	1 Sample(s) Required between 1/12/2020 and 1/18/2020
	1 Sample(s) Required between 1/26/2020 and 2/1/2020
	1 Sample(s) Required between 2/9/2020 and 2/15/2020
	1 Sample(s) Required between 2/23/2020 and 2/29/2020
	1 Sample(s) Required between 3/8/2020 and 3/14/2020
	1 Sample(s) Required between 3/22/2020 and 3/28/2020
	1 Sample(s) Required between 4/5/2020 and 4/11/2020
	1 Sample(s) Required between 4/19/2020 and 4/25/2020
	1 Sample(s) Required between 5/3/2020 and 5/9/2020
	1 Sample(s) Required between 5/17/2020 and 5/23/2020
	1 Sample(s) Required between 5/31/2020 and 6/6/2020
	1 Sample(s) Required between 6/14/2020 and 6/20/2020
	1 Sample(s) Required between 6/28/2020 and 7/4/2020
	1 Sample(s) Required between 7/12/2020 and 7/18/2020
	1 Sample(s) Required between 7/26/2020 and 8/1/2020
	1 Sample(s) Required between 8/9/2020 and 8/15/2020
	1 Sample(s) Required between 8/23/2020 and 8/29/2020
	1 Sample(s) Required between 9/6/2020 and 9/12/2020
	1 Sample(s) Required between 9/20/2020 and 9/26/2020
1 Sample(s) Required between 10/4/2020 and 10/10/2020	
1 Sample(s) Required between 10/18/2020 and 10/24/2020	
1 Sample(s) Required between 11/1/2020 and 11/7/2020	
1 Sample(s) Required between 11/15/2020 and 11/21/2020	
1 Sample(s) Required between 11/29/2020 and 12/5/2020	
1 Sample(s) Required between 12/13/2020 and 12/19/2020	

Cyanobacteria screening sample is to be collected biweekly from raw source water at sample point LT2001 unless requirements for reduced monitoring are met. Current reduced monitoring schedules can be found at <http://epa.ohio.gov/ddagw/HAB.aspx>. As of 12/31/17, all public water systems are responsible for contracting with a lab certified to perform cyanobacteria screening (qPCR). Please review the website for further information pertaining to follow-up sampling requirements for cyanobacteria screening gene detections, and certified labs that can perform analysis.



OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS000	Facility Name: WILMINGTON, CITY OF DISTRIBUTION	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

ASBESTOS - 1094 1 Sample(s) Required between 1/1/2020 and 5/31/2020

Collect one sample at a tap served by asbestos-cement pipe. Due to limited Laboratory capacity and a 48 hour filtering requirement, contact your lab early in the monitoring period to schedule a sampling date.

TOTAL COLIFORM (TCR) - 3100

10 Sample(s) Required between 1/1/2020 and 1/31/2020

10 Sample(s) Required between 2/1/2020 and 2/29/2020

10 Sample(s) Required between 3/1/2020 and 3/31/2020

10 Sample(s) Required between 4/1/2020 and 4/30/2020

10 Sample(s) Required between 5/1/2020 and 5/31/2020

10 Sample(s) Required between 6/1/2020 and 6/30/2020

10 Sample(s) Required between 7/1/2020 and 7/31/2020

10 Sample(s) Required between 8/1/2020 and 8/31/2020

10 Sample(s) Required between 9/1/2020 and 9/30/2020

10 Sample(s) Required between 10/1/2020 and 10/31/2020

10 Sample(s) Required between 11/1/2020 and 11/30/2020

10 Sample(s) Required between 12/1/2020 and 12/31/2020

TOTAL CHLORINE - 1000

10 Sample(s) Required between 1/1/2020 and 1/31/2020

10 Sample(s) Required between 2/1/2020 and 2/29/2020

10 Sample(s) Required between 3/1/2020 and 3/31/2020

10 Sample(s) Required between 4/1/2020 and 4/30/2020

10 Sample(s) Required between 5/1/2020 and 5/31/2020

10 Sample(s) Required between 6/1/2020 and 6/30/2020

10 Sample(s) Required between 7/1/2020 and 7/31/2020

10 Sample(s) Required between 8/1/2020 and 8/31/2020

10 Sample(s) Required between 9/1/2020 and 9/30/2020

10 Sample(s) Required between 10/1/2020 and 10/31/2020

10 Sample(s) Required between 11/1/2020 and 11/30/2020

10 Sample(s) Required between 12/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 300 OAK DR.	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS

Dual Sample Required between 1/8/2020 and 1/14/2020 at: DS201

Dual Sample Required between 4/8/2020 and 4/14/2020 at: DS201

Dual Sample Required between 7/8/2020 and 7/14/2020 at: DS201



OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 300 OAK DR.	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 10/8/2020 and 10/14/2020 at: DS201

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 3992 ST 730	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 1/8/2020 and 1/14/2020 at: DS202
	Dual Sample Required between 4/8/2020 and 4/14/2020 at: DS202
	Dual Sample Required between 7/8/2020 and 7/14/2020 at: DS202
	Dual Sample Required between 10/8/2020 and 10/14/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: DS203	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 863 S. SOUTH ST.	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 1/8/2020 and 1/14/2020 at: DS203
	Dual Sample Required between 4/8/2020 and 4/14/2020 at: DS203
	Dual Sample Required between 7/8/2020 and 7/14/2020 at: DS203
	Dual Sample Required between 10/8/2020 and 10/14/2020 at: DS203

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: DS204	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 4425 SR 730	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 1/8/2020 and 1/14/2020 at: DS204
	Dual Sample Required between 4/8/2020 and 4/14/2020 at: DS204
	Dual Sample Required between 7/8/2020 and 7/14/2020 at: DS204



Effective Date: 01/01/2020

2020 DISTRIBUTION SCHEDULE

OH1401211 WILMINGTON CITY PWS

System Type: Community

Operating Period: 1/1 to 12/31

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

** REMINDER: ** Consumer Confidence Report (CCR) is due July 1, 2020

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS204	Facility Name: WILMINGTON, CITY OF DISTRIBUTION 4425 SR 730	Facility Class: CLASS 1
--------------------------	---	--	--------------------------------

Chemicals Monitoring Requirements

DISINFECTION BYPRODUCTS Dual Sample Required between 10/8/2020 and 10/14/2020 at: DS204

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) - 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: LC###	Facility Name: WILMINGTON, CITY OF DISTRIBUTION Refer to your Lead and Copper plan for SMP IDs	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals Monitoring Requirements

LEAD - 1030 AND COPPER - 1022 Not Required



OH1432112 EAST CLINTON HIGH SCHOOL

System Type: Nontransient Noncommunity

Operating Period: 1/1 to 12/31

ENTRY POINT MONITORING SCHEDULE

Sampling Location	Facility ID: 1453388	Facility Name: EAST CLINTON HIGH SCHOOL	Facility Class: CLASS 1
	SMP ID: EP001	Facility Source: Ground Water	

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

Chemicals	Monitoring Requirements
ARSENIC - 1005	1 Sample(s) Required between 1/1/2020 and 3/31/2020 1 Sample(s) Required between 4/1/2020 and 6/30/2020 1 Sample(s) Required between 7/1/2020 and 9/30/2020 1 Sample(s) Required between 10/1/2020 and 12/31/2020
INORGANICS	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
ANTIMONY, TOTAL - 1074 BARIUM - 1010 BERYLLIUM, TOTAL - 1015 CADMIUM - 1015 CHROMIUM - 1020 CYANIDE - 1024 FLUORIDE - 1025 MERCURY - 1035 NICKEL - 1036 SELENIUM - 1045 THALLIUM, TOTAL	
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 5/31/2020
SYNTHETIC ORGANIC CHEMICALS (SOC) GROUP 1	1 Sample(s) Required between 1/1/2020 and 5/31/2020
<i>Sample for all the analytes listed below:</i>	
ALACHLOR (LASSO) - 2051 ATRAZINE - 2050 SIMAZINE - 2037	
VOLATILE ORGANIC CHEMICALS (VOC)	1 Sample(s) Required between 7/1/2020 and 9/30/2020

OH1432112 EAST CLINTON HIGH SCHOOL

System Type: Nontransient Noncommunity

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1 SMP ID: DS000	Facility Name: EAST CLINTON HIGH SCHOOL DISTRIBUTION	Facility Class: CLASS 1
--------------------------	---	---	--------------------------------

Chemicals	Monitoring Requirements
TOTAL COLIFORM (TCR) - 3100	1 Sample(s) Required between 1/1/2020 and 3/31/2020 1 Sample(s) Required between 4/1/2020 and 6/30/2020 1 Sample(s) Required between 7/1/2020 and 9/30/2020 1 Sample(s) Required between 10/1/2020 and 12/31/2020
TOTAL CHLORINE - 1000	1 Sample(s) Required between 1/1/2020 and 3/31/2020 1 Sample(s) Required between 4/1/2020 and 6/30/2020 1 Sample(s) Required between 7/1/2020 and 9/30/2020 1 Sample(s) Required between 10/1/2020 and 12/31/2020

Samples should be collected at the same time and place as the Total Coliform samples.

Sampling Location	Facility ID: DS1 SMP ID: DS201	Facility Name: EAST CLINTON HIGH SCHOOL DISTRIBUTION	Facility Class: CLASS 1
ADDRESS NOT KNOWN			

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 3/8/2020 and 3/14/2020 at: DS201 Dual Sample Required between 6/8/2020 and 6/14/2020 at: DS201 Dual Sample Required between 9/8/2020 and 9/14/2020 at: DS201 Dual Sample Required between 12/8/2020 and 12/14/2020 at: DS201

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950

Sampling Location	Facility ID: DS1 SMP ID: DS202	Facility Name: EAST CLINTON HIGH SCHOOL DISTRIBUTION	Facility Class: CLASS 1
ADDRESS NOT KNOWN			

Chemicals	Monitoring Requirements
DISINFECTION BYPRODUCTS	Dual Sample Required between 3/8/2020 and 3/14/2020 at: DS202 Dual Sample Required between 6/8/2020 and 6/14/2020 at: DS202 Dual Sample Required between 9/8/2020 and 9/14/2020 at: DS202 Dual Sample Required between 12/8/2020 and 12/14/2020 at: DS202

Sample for all the analytes listed below:

- 1) TOTAL HALOACETIC ACIDS (HAA5) – 2456
- 2) TTHM - 2950



Effective Date: 01/01/2020

2020 DISTRIBUTION SCHEDULE

OH1432112 EAST CLINTON HIGH SCHOOL

System Type: Nontransient Noncommunity

Operating Period: 1/1 to 12/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule.

Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

DISTRIBUTION MONITORING SCHEDULE

Sampling Location	Facility ID: DS1	Facility Name: EAST CLINTON HIGH SCHOOL DISTRIBUTION	Facility Class: CLASS 1
	SMP ID: LC###	Refer to your Lead and Copper plan for SMP IDs	

Chemicals

Monitoring Requirements

LEAD - 1030 AND COPPER - 1022

10 Sample(s) Required between 6/1/2020 and 9/30/2020

Lead consumer notice must be completed no later than two business days after receipt of the sample results. The verification form for consumer notice must be submitted to Ohio EPA no later than five business days after receipt of the sample results. Lead and copper sample monitoring point (SMP) IDs (LC###) must be current and reflect properly tiered sites according to OAC Rule 3745-81-86. Submit lead and copper SMP ID revisions to your Ohio EPA District Office. Forms and templates are available online at <http://epa.ohio.gov/ddagw/pws/leadandcopper.aspx>. For questions contact your Ohio EPA District Office representative.

OH1434012 BEECHWOOD ACRES

System Type: Transient Noncommunity

Operating Period: 5/1 to 10/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378


DISTRIBUTION MONITORING SCHEDULE

Sampling Facility ID: DS1 Facility Name: BEECHWOOD ACRES DISTRIBUTION
Location SMP ID: SUP01 Facility Source: Ground Water

Chemicals	Monitoring Requirements
TOTAL COLIFORM - SEASONAL STARTUP	At least 1 negative Total Coliform Bacteria sample prior to serving water to the public

*** Seasonal start-up sample does not count for routine compliance requirements. Collect at least one special purpose (SP) sample for total coliform (TC) analysis at the service connection considered to be most susceptible to contamination. The sample must be TC negative before the system may serve water to the public. If the sample is positive, contact your Ohio EPA District Representative for additional requirements. If your start date is different from last year, please contact your Ohio EPA District Representative.***

Where to Collect Samples For a Small Public Water System

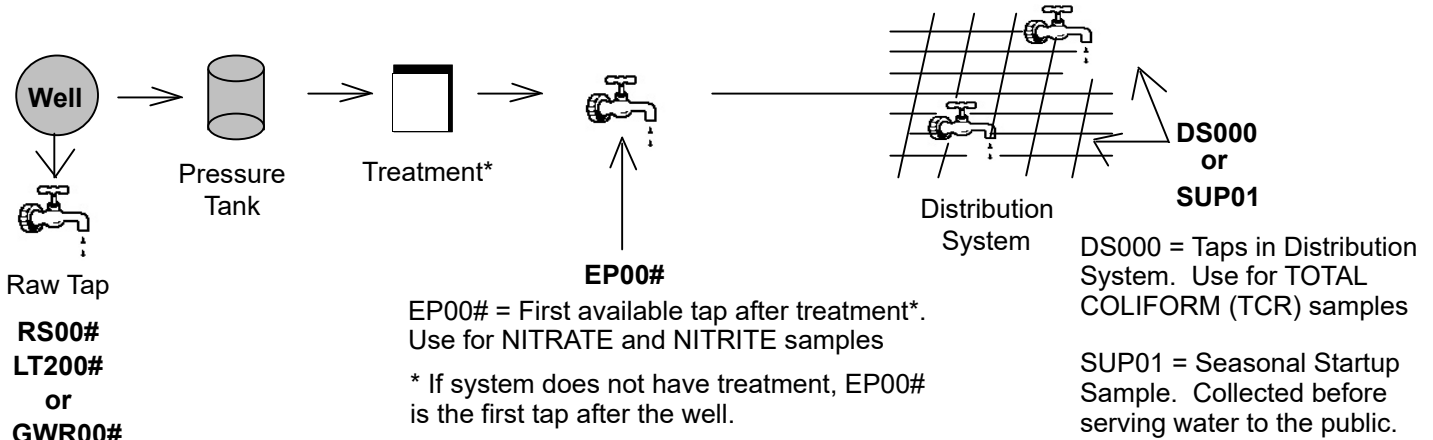

Failing to sample for total coliform or nitrate will cost you \$150 or more in penalties for each monitoring violation. A list of drinking water sample collection services that can assist you with collecting water samples is located at: <http://epa.ohio.gov/portals/28/documents/PWS/DWSample.pdf>.

Save a dime. Sample on time!

OH1434012 BEECHWOOD ACRES

System Type: Transient Noncommunity

Operating Period: 5/1 to 10/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.


For water emergencies that occur after hours, please call 800-282-9378

DISTRIBUTION MONITORING SCHEDULE

Sampling Facility ID: DS1	Facility Name: BEECHWOOD ACRES DISTRIBUTION
Location SMP ID: DS000	Facility Source: Ground Water

Chemicals	Monitoring Requirements
TOTAL COLIFORM (TCR) - 3100	1 Sample(s) Required between 5/21/2020 and 5/31/2020
	1 Sample(s) Required between 6/1/2020 and 6/30/2020
	1 Sample(s) Required between 7/1/2020 and 7/31/2020
	1 Sample(s) Required between 8/1/2020 and 8/31/2020
	1 Sample(s) Required between 9/1/2020 and 9/30/2020
	1 Sample(s) Required between 10/1/2020 and 10/31/2020

Where to Collect Samples For a Small Public Water System

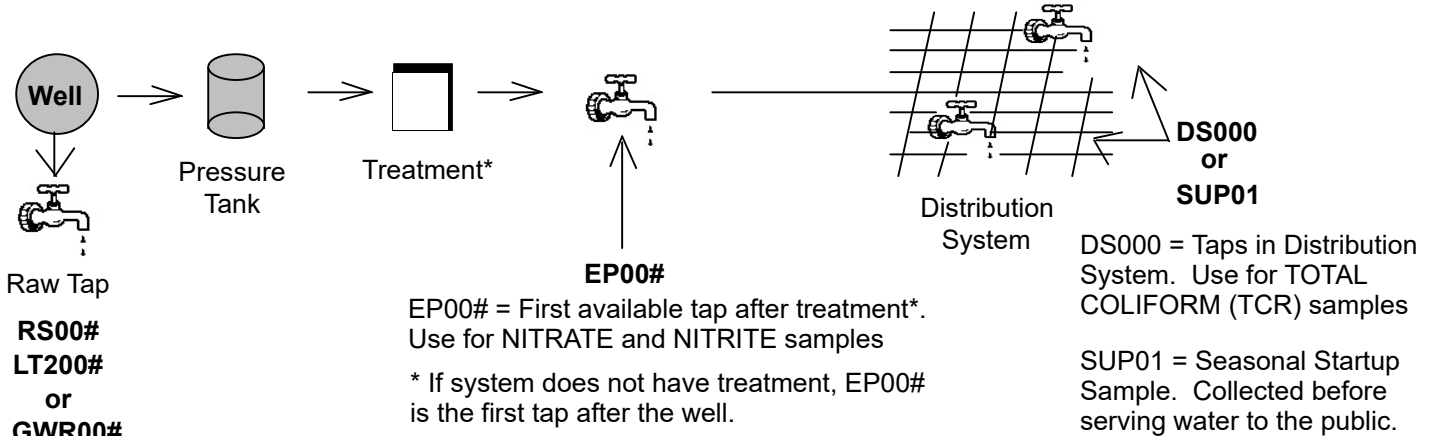

Failing to sample for total coliform or nitrate will cost you \$150 or more in penalties for each monitoring violation. A list of drinking water sample collection services that can assist you with collecting water samples is located at: <http://epa.ohio.gov/portals/28/documents/PWS/DWSample.pdf>.

Save a dime. Sample on time!

OH1434012 BEECHWOOD ACRES

System Type: Transient Noncommunity

Operating Period: 5/1 to 10/31

Ground Water Rule Substantial System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

ENTRY POINT MONITORING SCHEDULE

Sampling Facility ID: 1453391 Facility Name: BEECHWOOD ACRES
Location SMP ID: EP001 Facility Source: Ground Water

Chemicals	Monitoring Requirements
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 5/31/2020

Where to Collect Samples For a Small Public Water System



Failing to sample for total coliform or nitrate will cost you \$150 or more in penalties for each monitoring violation. A list of drinking water sample collection services that can assist you with collecting water samples is located at: <http://epa.ohio.gov/portals/28/documents/PWS/DWSample.pdf>.

Save a dime. Sample on time!

OH1434812 COMMUNITY CHRISTIAN CHURCH

System Type: Transient Noncommunity

Operating Period: 1/1 to 12/31

Ground Water Rule Minimal Treatment System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

DISTRIBUTION MONITORING SCHEDULE

Sampling Facility ID: **DS1** Facility Name: **COMMUNITY CHRISTIAN CHUR DISTRIBUTION**
Location SMP ID: **DS000** Facility Source: **Ground Water**

Chemicals	Monitoring Requirements
TOTAL COLIFORM (TCR) - 3100	1 Sample(s) Required between 1/1/2020 and 3/31/2020
	1 Sample(s) Required between 4/1/2020 and 6/30/2020
	1 Sample(s) Required between 7/1/2020 and 9/30/2020
	1 Sample(s) Required between 10/1/2020 and 12/31/2020

Where to Collect Samples For a Small Public Water System



Failing to sample for total coliform or nitrate will cost you \$150 or more in penalties for each monitoring violation. A list of drinking water sample collection services that can assist you with collecting water samples is located at: <http://epa.ohio.gov/portals/28/documents/PWS/DWSample.pdf>.

Save a dime. Sample on time!

OH1434812 COMMUNITY CHRISTIAN CHURCH

System Type: Transient Noncommunity

Operating Period: 1/1 to 12/31

Ground Water Rule Minimal Treatment System

THIS SCHEDULE MAY NOT INCLUDE ALL MONITORING REQUIREMENTS FOR YOUR SYSTEM.

Contact your district office to review additional monitoring for operating parameters, and/or other monitoring requirements not included on this schedule. Also, monitoring schedules may be revised during the year based on sampling results.

For water emergencies that occur after hours, please call 800-282-9378

ENTRY POINT MONITORING SCHEDULE

Sampling Facility ID: 1453393 Facility Name: COMMUNITY CHRISTIAN CHURCH
Location SMP ID: EP001 Facility Source: Ground Water

Chemicals	Monitoring Requirements
NITRITE - 1041	1 Sample(s) Required between 1/1/2020 and 5/31/2020
NITRATE - 1040	1 Sample(s) Required between 1/1/2020 and 5/31/2020

Where to Collect Samples For a Small Public Water System



Failing to sample for total coliform or nitrate will cost you \$150 or more in penalties for each monitoring violation. A list of drinking water sample collection services that can assist you with collecting water samples is located at: <http://epa.ohio.gov/portals/28/documents/PWS/DWSample.pdf>.

Save a dime. Sample on time!
